

SAN MATEO COUNTY COMMUNITY COLLEGE DISTRICT

Capital Improvement Program Status Report

Bond Oversight Committee May 19, 2008








Cañada College Gateways/Circulation /Parking Project

Construction phase: June 2008 – May 2009

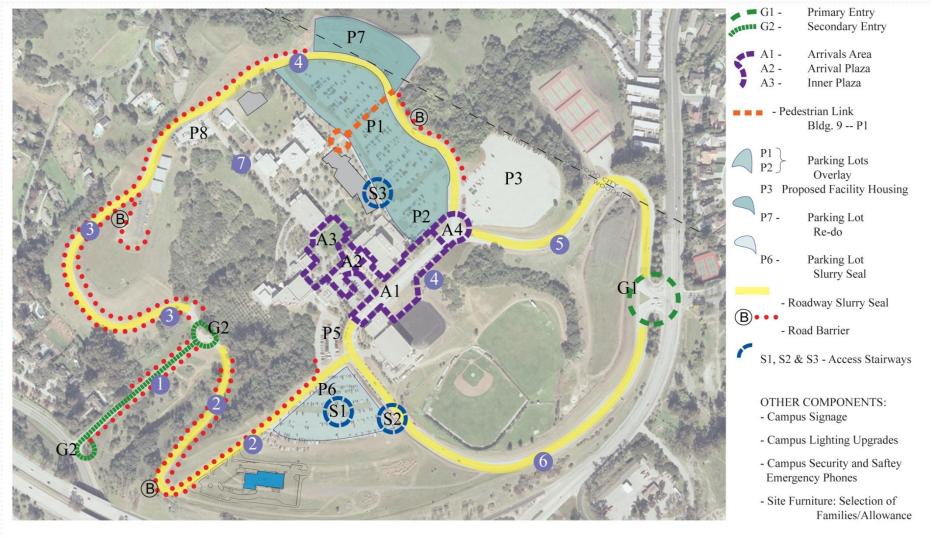

Cañada College Gateways/Circulation/Parking Project

Selection of Design-Builder

- District Staff prequalified six Design Builders to submit proposals for this project
- District Staff and Swinerton Management & Consulting reviewed the five proposals submitted from the prequalified Design Builders to score their responsiveness to the Request for Proposal

	Evaluation Factor	Maximum Possible Score	Robert A. Bothman, Inc.	Big-D Pacific Builders	John Plane Construction	Schembri Construction	ValleyCrest
1.	Price	40	39	35	33	37	37
2.	Project Management Plan	20	18	14	11	18	10
3.	Technical Expertise	10	8	8	6	8	7
4.	Acceptable Safety Record	10	9	4	6	9	7
5.	Skilled Labor Force Availability	10	8	9	6	9	4
6.	Life Cycle Costs over 25 years	10	10	10	10	10	10
	TOTALS	100	92	80	72	91	75

• Summary of the reviewer's assessment and scoring of the five proposals:

- The District interviewed the top two ranked Design Builders in late April and early May, who were allowed the opportunity to present their best and final proposals
- Staff performed due diligence on these final proposals with focus on price, project schedule and management plan, and company history
- Based on this evaluation, the panel recommended that the Board of Trustees award the Design-Build Contract to Robert A. Bothman, Inc.
- On May 14, 2008 the Board approved the Contract Award



Cañada College Gateways Project Schedule


3 Parking Lc 4 Lot 11 5 Lot 12 7 Lot 24 7 Lot 6 8 Lot 7 9 Lot 11 10 Lot 14 11 Replay 12 Lighting W 13 Bidg. 5 14 Athledt 15 Arrival Zor 16 Arrival 17 Arrival 18 Replay 20 Arrival 21 Arrival 22 Arrival 23 Arrival	uration (To Substantial Completion Its South South South (Alt. #5) Alt.#7) edestrian Walkway & 2 Stairs & Parking Lot 4 (V.Alt.#) Fork Cork Cork Cried Lighting (Alt.#9) Cork Ese Zone 1 Zone 2 Water Valves (Alt.#14) Zone 3 Zone 7	0 days 195 days 158 days 55 days 55 days 42 days 42 days 15 days 20 days 18 days 20 days 30 days 30 days 22 days 8 days 40 days	Mon 6/2/08 Mon 6/2/08 Mon 6/2/08 Mon 8/2/08 Mon 8/18/08 Mon 8/18/08 Mon 8/18/08 Mon 8/18/08 Mon 8/18/08 Mon 9/8/08 Mon 6/2/08 Mon 6/2/08 Mon 6/2/08 Mon 6/2/08	Mon 6/2/08 Fri 2/27/09 Wed 17/79 Fri 8/15/08 Tue 10/14/08 Fri 10/14/08 Fri 10/14/08 Fri 10/3/08 Wed 1/7/09 Fri 7/25/08 Fri 6/27/08 Fri 6/27/08 Fri 7/25/08 Fri 7/25/08 Fri 7/25/08	Notice to Proceed @/19/08 Construction Duration (To Substantial Comp Parking Lots Parking Lots Parking Lots Lot 1 North Lot 1 South Lot 2 Lighting (Alt. #5) Lot 6 (Alt #7) Lot 1 Pedestrian Walkway Lot 1 Pedestrian Walkway Lot 1 & 2 Stairs Replace Parking Lot 4 (V.Alt. #) Bidg. 5 & 6 Lighting (Alt. #9) Athletic Field Lighting (Alt. #8)
Parking Lo Image: Constraint of the second secon	V15 Jorth South Jighting (Alt. #5) Alt #7) edestrian Walkway & 2 Stairs se Parking Lot 4 (V.Alt. #) fork c Field Lighting (Alt. #9) c Field Lighting (Alt. #8) tes Zone 1 Zone 2 :e Water Valves (Alt. #14) Zone 7	158 days 55 days 55 days 42 days 42 days 15 days 20 days 20 days 20 days 40 days 20 days 30 days 22 days 8 days	Mon 6/2/08 Mon 8/18/08 Mon 8/18/08 Mon 8/18/08 Mon 8/18/08 Mon 8/18/08 Mon 9/8/08 Mon 12/15/08 Mon 6/2/08 Mon 6/2/08 Mon 6/2/08	Fri 8/15/08 Fri 8/15/08 Tue 10/14/08 Tue 10/14/08 Fri 10/17/08 Fri 10/3/08 Wed 1/7/09 Fri 7/25/08 Fri 6/27/08 Fri 6/27/08	Parking Lots Parki
Lut 11 Lut 11 Lut 1 Lut	North South Jighting (Alt. #5) Alt #7) edestrian Walkway & 2 Stairs e Parking Lot 4 (V.Alt. #) fork 5 & 6 Lighting (Alt. #9) c Field Lighting (Alt. #9) c Field Lighting (Alt. #8) tes Zone 1 Zone 2 e Water Valves (Alt. #14) Zone 3 Zone 7	55 days 55 days 42 days 42 days 45 days 15 days 20 days 18 days 20 days 30 days 22 days 8 days	Mon 6/2/08 Mon 8/18/08 Mon 8/18/08 Mon 8/18/08 Mon 8/18/08 Mon 8/18/08 Mon 9/8/08 Mon 6/2/08 Mon 6/2/08 Mon 6/2/08	Fri 8/15/08 Tue 10/14/08 Tue 10/14/08 Fri 10/17/08 Fri 10/3/08 Wed 1/7/09 Fri 7/25/08 Fri 6/27/08 Fri 7/25/08	Lot 1 North Lot 1 South Lot 2 Lighting (Alt. #5) Lot 6 (Alt #7) Lot 7 Lot 1 Pedestrian Walkway Lot 1 & 2 Stairs Feplace Parking Lot 4 (V.Alt. #) Bidg. 5 & 6 Lighting (Alt. #9) Athletic Field Lighting (Alt. #8)
Luci 2 I Luci 2 I Luci 6 (Luci 7 Luci 1 F Bella Bella 8 Bella 9 Content 1 Content 1 C	ighting (Alt. #5) Alt #7) edestrian Walkway 2 2 Stairs te Parking Lot 4 (V.Alt. #) fork 5 8 6 Lighting (Alt. #9) c Field Lighting (Alt. #9) c Field Lighting (Alt. #8) tes Zone 1 Zone 2 te Water Valves (Alt. #14) Zone 3 Zone 7	55 days 42 days 42 days 45 days 15 days 20 days 18 days 40 days 20 days 20 days 18 days 20 days 20 days 20 days 30 days 30 days 22 days 8 days	Mon 6/2/08 Mon 8/18/08 Mon 8/18/08 Mon 8/18/08 Mon 8/18/08 Mon 8/18/08 Mon 9/8/08 Mon 6/2/08 Mon 6/2/08 Mon 6/2/08	Tue 10/14/08 Tue 10/14/08 Fri 10/17/08 Fri 10/17/08 Fri 10/3/08 Wed 1/7/09 Fri 7/25/08 Fri 6/27/08 Fri 7/25/08 Wed 1/21/09	Lot 1 South Lot 2 Lighting (Alt. #5) Lot 6 (Alt #7) Lot 7 Lot 7 Lot 1 Pedestrian Walkway Lot 1 & 2 Stairs Fieplace Parking Lot 4 (V.Alt. #) Bidg. 5 & 6 Lighting (Alt. #9) Athletic Field Lighting (Alt. #8)
Lut 2 I Lut 2 I Lut 6 (Lut 7 Lut 17 Bepla Lut 14 Bepla Lighting W Bidg. Athleti Arrival Arriv	ighting (Alt. #5) Alt #7) edestrian Walkway 2 2 Stairs te Parking Lot 4 (V.Alt. #) fork 5 8 6 Lighting (Alt. #9) c Field Lighting (Alt. #9) c Field Lighting (Alt. #8) tes Zone 1 Zone 2 te Water Valves (Alt. #14) Zone 3 Zone 7	42 days 42 days 45 days 15 days 20 days 18 days 20 days 20 days 20 days 30 days 22 days 8 days	Mon 8/18/08 Mon 8/18/08 Mon 8/18/08 Mon 8/18/08 Mon 9/8/08 Mon 9/8/08 Mon 6/2/08 Mon 6/2/08 Mon 6/2/08	Tue 10/14/08 Tue 10/14/08 Fri 10/17/08 Fri 10/17/08 Fri 10/3/08 Wed 1/7/09 Fri 7/25/08 Fri 6/27/08 Fri 7/25/08 Wed 1/21/09	Lighting (Alt. #5) Lot 6 (Alt #7) Lot 7 Lot 7 Lot 1 Pedestrian Walkway Lot 1 & 2 Stairs Feplace Parking Lot 4 (V.Alt. #) Bidg. 5 & 6 Lighting (Alt. #9) Athletic Field Lighting (Alt. #8)
Lot 6 (Lot 7 Lot 17 Lot 17 Replac Lighting M Bidg. Athleti Arrival Ar	Alt #7) edestrian Walkway & 2 Stairs the Parking Lot 4 (V.Alt. #) fork fork c Field Lighting (Alt. #9) c Field Lighting (Alt. #9) tes Zone 1 Zone 2 te Water Valves (Alt. #14) Zone 3 Zone 7	42 days 45 days 15 days 20 days 18 days 20 days 20 days 20 days 168 days 30 days 22 days 8 days	Mon 8/18/08 Mon 8/18/08 Mon 8/18/08 Mon 9/8/08 Mon 12/15/08 Mon 6/2/08 Mon 6/2/08 Mon 6/2/08	Tue 10/14/08 Fri 10/17/08 Fri 9/5/08 Fri 10/3/08 Wed 1/7/09 Fri 7/25/08 Fri 6/27/08 Fri 7/25/08 Wed 1/21/09	Lighting Work Bildg. 5 & 6 Lighting (Alt. #9) Athletic Field Lighting (Alt. #8)
Lut 7 Lut 17 Lut 18 Repla Lighting W Athlet Arrival Ar	edestrian Walkway & 2 Stairs be Parking Lot 4 (V.Alt. #) fork & 6 Lighting (Alt. #9) c Field Lighting (Alt. #8) tes Zone 1 Zone 2 be Water Valves (Alt. #14) Zone 3 Zone 7	45 days 15 days 20 days 18 days 20 days 20 days 20 days 20 days 20 days 30 days 22 days 8 days	Mon 8/18/08 Mon 9/8/08 Mon 12/15/08 Mon 6/2/08 Mon 6/2/08 Mon 6/2/08 Mon 6/2/08	Fri 10/17/08 Fri 9/5/08 Fri 10/3/08 Wed 1/7/09 Fri 7/25/08 Fri 6/27/08 Fri 7/25/08 Wed 1/21/09	Lot 7 Lot 1 Pedestrian Walkway Lot 1 & 2 Stairs Replace Parking Lot 4 (V.Alt. #) Bidg. 5 & 6 Lighting (Alt. #9) Athletic Field Lighting (Alt. #8)
D Lot 1 8 Replac Replac Lighting W Bidg. 5 Arrival Arrival Zor Arrival Arrival Statirs Statirs	A 2 Stairs = Parking Lot 4 (V.Alt. #) fork 5 & 6 Lighting (Alt. #9) = Field Lighting (Alt. #8) == Zone 1 Zone 2 == Water Valves (Alt. #14) Zone 3 Zone 7	15 days 20 days 18 days 40 days 20 days 20 days 168 days 30 days 22 days 8 days 20 days 168 days 30 days 22 days 8 days	Mon 9/8/08 Mon 12/15/08 Mon 6/2/08 Mon 6/2/08 Mon 6/30/08 Mon 6/2/08 Mon 6/2/08	Fri 10/3/08 Wed 1/7/09 Fri 7/25/08 Fri 6/27/08 Fri 7/25/08 Wed 1/21/09	Lighting Work Bidg. 5 & 6 Lighting (Alt. #9) Athletic Field Lighting (Alt. #8)
Lot 1 4 Replace Lighting W Bidg. 5 Artival Zor Arrival Replace Arrival	A 2 Stairs = Parking Lot 4 (V.Alt. #) fork 5 & 6 Lighting (Alt. #9) = Field Lighting (Alt. #8) == Zone 1 Zone 2 == Water Valves (Alt. #14) Zone 3 Zone 7	20 days 18 days 40 days 20 days 20 days 168 days 30 days 22 days 8 days	Mon 12/15/08 Mon 6/2/08 Mon 6/2/08 Mon 6/30/08 Mon 6/2/08 Mon 6/2/08	Wed 1/7/09 Fri 7/25/08 Fri 6/27/08 Fri 7/25/08 Wed 1/21/09	Lighting Work Bldg. 5 & 6 Lighting (Alt. #9) Athletic Field Lighting (Alt. #8)
Lighting W Bidg. 4 Arhiet Arrival Zor Arrival Arrival Arrival Arrival Arrival Arrival Arrival Arrival Arrival Arrival Stairs	York 5 & 6 Lighting (Alt. #9) c Field Lighting (Alt. #8) tes Zone 1 Zone 2 e Water Valves (Alt. #14) Zone 3 Zone 7	18 days 40 days 20 days 20 days 168 days 30 days 22 days 8 days	Mon 6/2/08 Mon 6/2/08 Mon 6/30/08 Mon 6/2/08 Mon 6/2/08	Fri 7/25/08 Fri 6/27/08 Fri 7/25/08 Wed 1/21/09	Big. 5 & 6 Lighting (Alt. #9) Athletic Field Lighting (Alt. #8)
Bidg. 1 Athleti Arrival Zor Arrival Ar	5 & 6 Lighting (Alt. #9) c Field Lighting (Alt. #8) es Zone 1 Zone 2 e Water Valves (Alt. #14) Zone 3 Zone 7	20 days 20 days 168 days 30 days 22 days 8 days	Mon 6/2/08 Mon 6/30/08 Mon 6/2/08 Mon 6/2/08	Fri 6/27/08 Fri 7/25/08 Wed 1/21/09	Lighting Work Bldg. 5 & 6 Lighting (Alt. #9) Athletic Field Lighting (Alt. #8)
Athleti Arrival Zor Arrival Arrival Repla Arrival Arri	c Field Lighting (Alt. #8) tes Zone 1 Zone 2 zow 2 Zone 3 Zone 7	20 days 168 days 30 days 22 days 8 days	Mon 6/30/08 Mon 6/2/08 Mon 6/2/08	Fri 7/25/08 Wed 1/21/09	Bidg. 5 & 6 Lighting (Alt. #9) Athletic Field Lighting (Alt. #8)
Arrival Zor Arrival Pepla Arrival Arrival Arrival Arrival Arrival Arrival Stairs	tes Zone 1 Zone 2 te Water Valves (Alt. #14) Zone 3 Zone 7	20 days 168 days 30 days 22 days 8 days	Mon 6/2/08 Mon 6/2/08	Wed 1/21/09	Landau and L
Arrival	Zone 1 Zone 2 :e Water Valves (Alt. #14) Zone 3 Zone 7	30 days 22 days 8 days	Mon 6/2/08		Landau and L
Arrival Replac Arrival Arrival Arrival Arrival Arrival Arrival Stairs	Zone 2 ce Water Valves (Alt. #14) Zone 3 Zone 7	22 days 8 days		Ed 7/11/09	
Repla Arrival Arrival Arrival Arrival Arrival Stairs	ze Water Valves (Alt. #14) Zone 3 Zone 7	8 days	Mon 6/2/08	FII //11/00	Arrival Zone
Arrival Arrival Arrival Arrival Arrival Arrival Stairs	Zone 3 Zone 7	8 days		Tue 7/1/08	Arrival Zone 2
Arrival Arrival Arrival Arrival Arrival Stairs	Zone 7	40 dave	Mon 6/2/08	Wed 6/11/08	Feplace Water Valves (Alt. #14)
Arrival Arrival Arrival Arrival Stairs		40 days	Mon 6/2/08	Fri 7/25/08	Arrival Zone 3
Arrival Arrival Arrival Arrival Stairs	Zone 4	60 days	Mon 6/2/08	Fri 8/22/08	Arrival Zone 7
Arrival Arrival Stairs	active t	15 days	Mon 8/25/08	Fri 9/12/08	Arrival Zone 4
Arrival Stairs	Zone 5	20 days	Mon 8/25/08	Fri 9/19/08	Arrival Zone 5
Stairs	Zone 6	80 days	Mon 8/25/08	Fri 12/12/08	Arrival Zone 6
	Zone 8 - Y intersection	28 days	Mon 12/15/08	Wed 1/21/09	Arrival Zone 8 - Y Intersection
Gateways	@ Building 2 (Alt. #11)	16 days	Mon 8/25/08	Mon 9/15/08	Stairs @ Building 2 (Alt. #11)
Water		135 days	Mon 8/25/08	Fri 2/27/09	Gateways
Water	Feature @ Primary Gateway (Alt #3)	40 days	Mon 8/25/08	Fri 10/17/08	Water Feature @ Primary Gateway (Alt #3)
	y Gateway	50 days	Mon 10/20/08	Fri 12/26/08	Primary Gateway
	dary Gateway	45 days	Mon 12/29/08	Fri 2/27/09	Secondary Gateway
	Barriers	16 days	Mon 12/29/08	Mon 1/19/09	Road Barriers
	oad Barriers - Phase 1 (Alt. #1)	8 days	Mon 12/29/08	Wed 1/7/09	Road Barriers - Phase 1 (Alt. #1)
	oad Barriers - Phase 2 (Alt. #2)	8 days	Thu 1/8/09	Mon 1/19/09	Road Barriers - Phase 2 (Alt. #2)
Signage		55 days	Mon 12/15/08	Fri 2/27/09	Signage
	trian & Vehicular Signage (Alt. #6)	50 days	Mon 12/15/08	Fri 2/20/09	Pedestrian & Vehicular Signage (Alt. #6)
	antial Completion	0 days	Fri 2/27/09	Fri 2/27/09	Substantial Completion 🔶 2/27
Loop Road		50 days	Mon 3/2/09	Fri 5/8/09	Loop Road
	/Re-Construction	20 days	Mon 3/2/09	Fri 3/27/09	Crack Seal/Re-Construction
Slurry Seal		15 days	Mon 3/30/09	Fri 4/17/09	Slurry Seal
Pavement	Markings	15 days	Mon 4/20/09	Fri 5/8/09	Pavement Markings

College of San Mateo CIP2 Design-Build Project

- ✓ New Building 5N Workforce and Wellness Center
- New Building 10N Student Services, Administration, Bookstore, Food Service, Instruction
- ✓ Demolition of Buildings 5, 6, 10, 11, 13, T1 and Kiosko
- Sitework Improvements: Gateways & Quad Improvements, Parking, Paving, Sidewalk, Roadways
- Design and Construction Period: Spring 2008 Summer 2011




Building 5N: Workforce and Wellness Center





Building 5N: First Floor

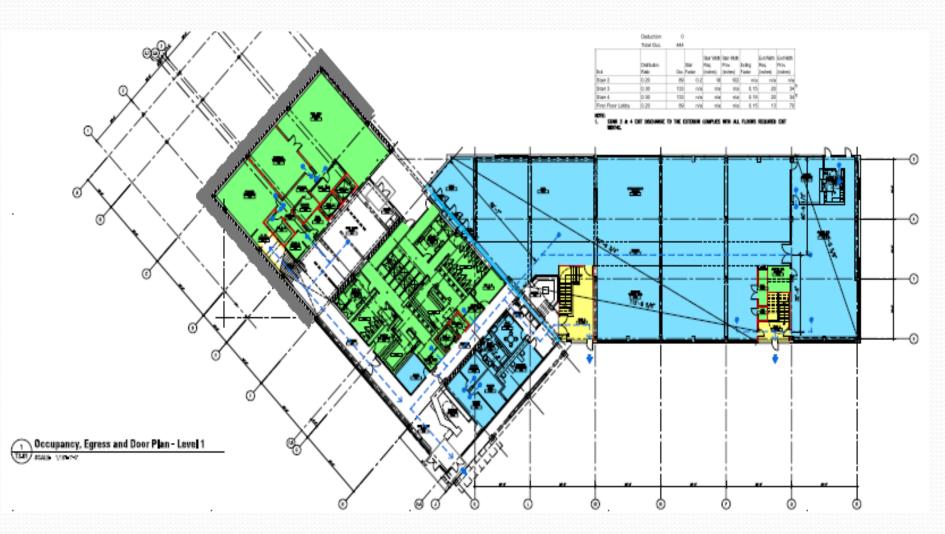


Building 5N: Second Floor




Building 5N: Third Floor



Building 10N: Administration and Student Services






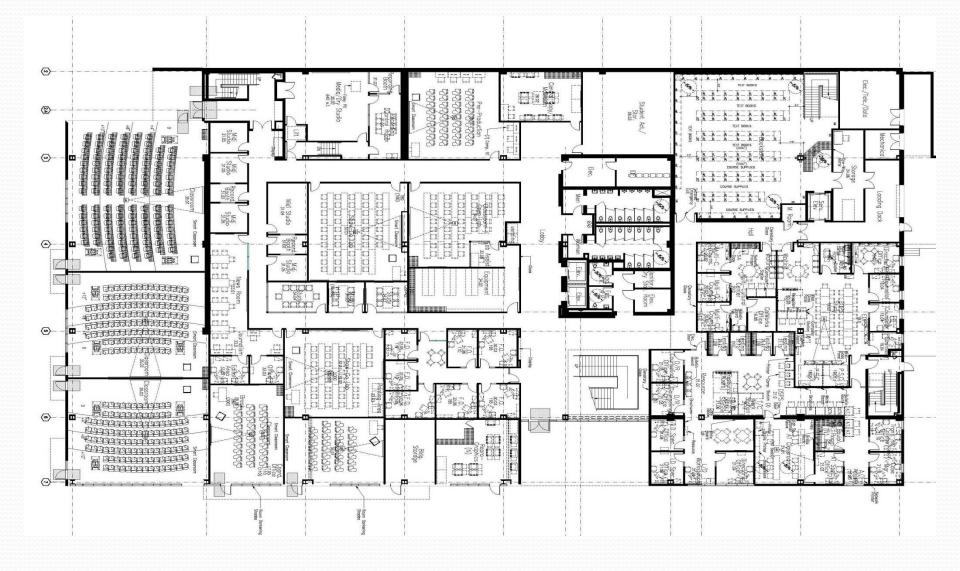


Building 10N: First Floor


Building 10N: Second Floor

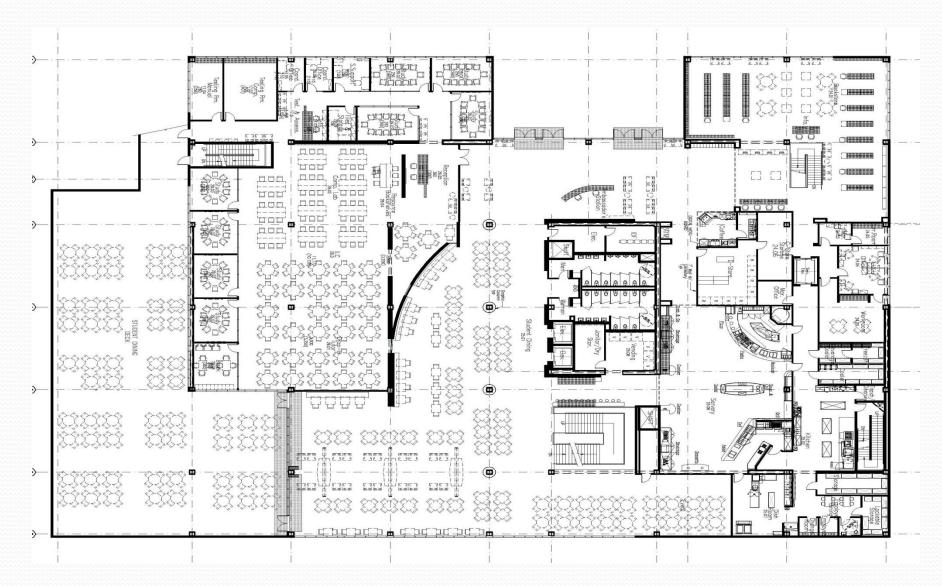


Building 10N: Third Floor

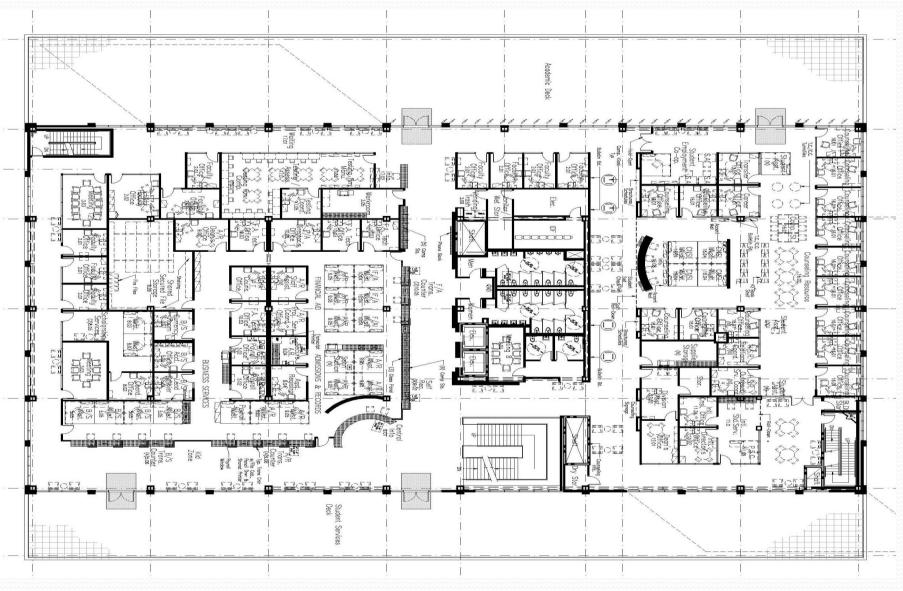

Building 10N: Fourth Floor

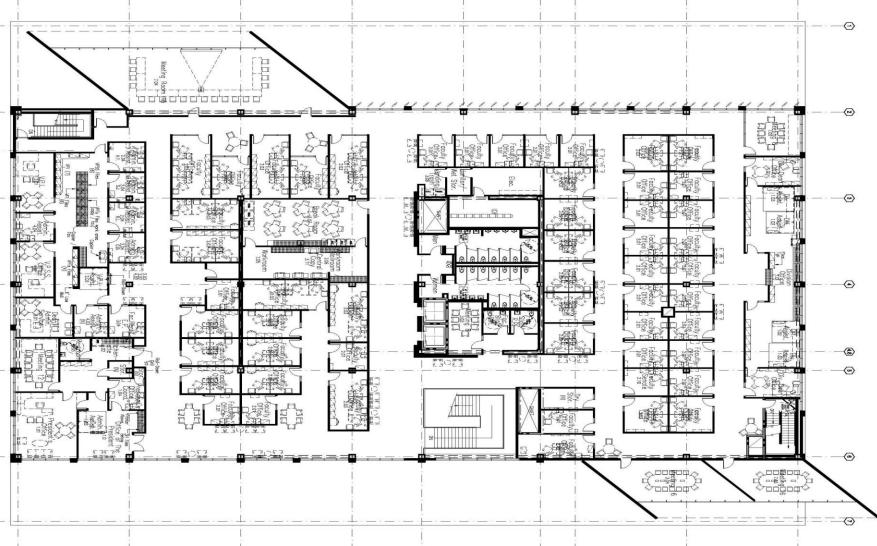

Sitework Improvements

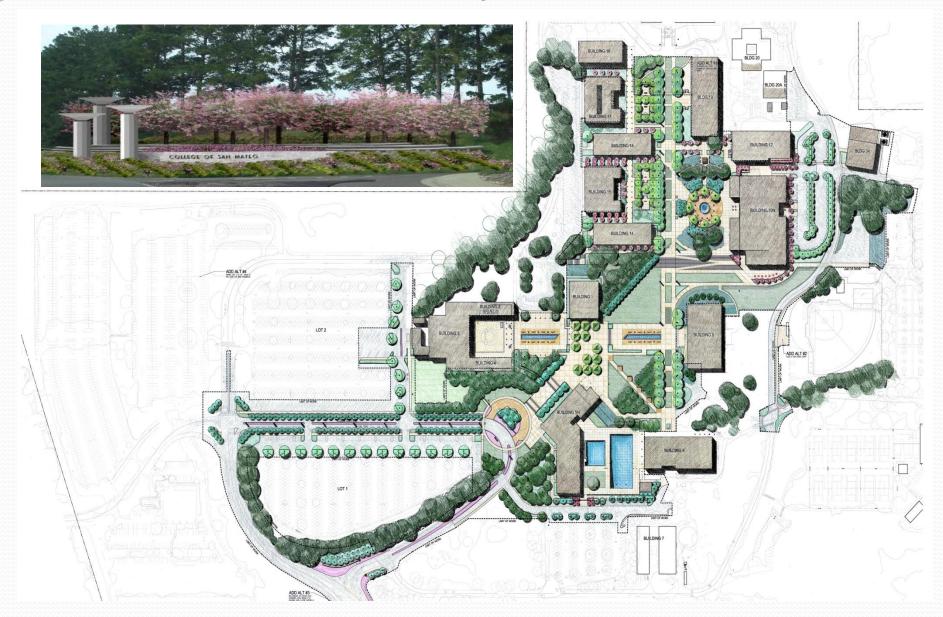

College of San Mateo CIP2 Design Build Project Schedule*

ID 1		0	Task Name	Duration	Start		aff 2nd Haif 1st Haif 1st Haif 2nd Haif 1st Haif
2							
2			CSM DESIGN-BUILD PROJECT	1109 days	Mon 6/25/07	Thu 9/22/11	CSM DESIGN-BUILD PROJECT
3			Preconstruction	340 days	Mon 6/25/07	Fri 10/10/08	Preconstruction
4	1		Request for Proposal Period	70 days	Mon 6/25/07	Fri 9/28/07	Request for Proposal Period
5	1		Proposal Evaluation & D-B Contract Award	60 days	Mon 10/1/07	Fri 12/21/07	Proposal Evaluation & D-B Contract Award
6	1		Design Period	210 days	Mon 12/24/07	Fri 10/10/08	Design Period
7	1		New B5N - Workforce/Wellness Center	100 days	Mon 12/24/07	Fri 5/9/08	New B5N - Workforce/Wellness Center
8	+		New B10N - Admin/Student Services	100 days	Mon 12/24/07	Fri 5/9/08	New B10N - Admin/Student Services
9	+		Sitework	210 days	Mon 12/24/07	Fri 10/10/08	Sitework
0			Site Utilities	130 days	Mon 12/24/07	Fri 6/20/08	Site Utilities
1	1		Construction	908 days	Tue 4/1/08	Thu 9/22/11	Construction
2			New B5N - Workforce/Wellness Center	604 days	Tue 4/1/08	Fri 7/23/10	New B5N - Workforce/Wellness Center
3		11	Relocate B5/6 occupants	33 days	Tue 4/1/08	Thu 5/15/08	Relocate B5/6 occupants
4	1		Demolition of existing B5/6 & pools	40 days	Fri 5/16/08	Thu 7/10/08	Demolition of existing B5/6 & pools
15	1		Construction	486 days	Fri 6/20/08	Fri 4/30/10	Construction
6	1		Group II FF&E installation	40 days	Mon 5/3/10	Fri 6/25/10	Group II FF&E installation
7	+		Commissioning & Faculty/Student transitioning	20 days	Mon 6/28/10	Fri 7/23/10	Commissioning & Faculty/Student transitioning
8			New B10N - Admin/Student Services	754 days	Mon 11/3/08	Thu 9/22/11	Vew B10N - Admin/Student Services
9	1		Demolition of existing B10 & B11	40 days	Mon 11/3/08	Fri 12/26/08	Demolition of existing B10 & B11
20	1		Construction	649 days	Mon 1/5/09	Thu 6/30/11	Construction
1			Group II FF&E installation	40 days	Fri 7/1/11	Thu 8/25/11	Group II FF&E installation
2			Commissioning & Faculty/Student transitioning	20 days	Fri 8/26/11	Thu 9/22/11	Commissioning & Faculty/Student transitioning
3			Site Improvements	875 days	Mon 4/14/08	Fri 8/19/11	Site Improvements
24	1	II.	Sitework	805 days	Mon 7/21/08	Fri 8/19/11	Sitework
25	+		Site Utilities	410 days	Mon 4/14/08	Fri 11/6/09	Site Utilities

Skyline College CIP₂ Design Build Project

- ✓ New Building 11N Auto Transmission
- ✓ New Building 4N Cosmetology, Administration and Wellness
- Sitework Improvements: Gateways & Quad Improvements, Parking, Paving, Sidewalk, Roadways
 - Design and Construction period: Spring 2008 Spring 2011




"Building Today for Education Tomorrow"

Building 4N: Cosmetology, Administration and Wellness







Building 4N: First Floor

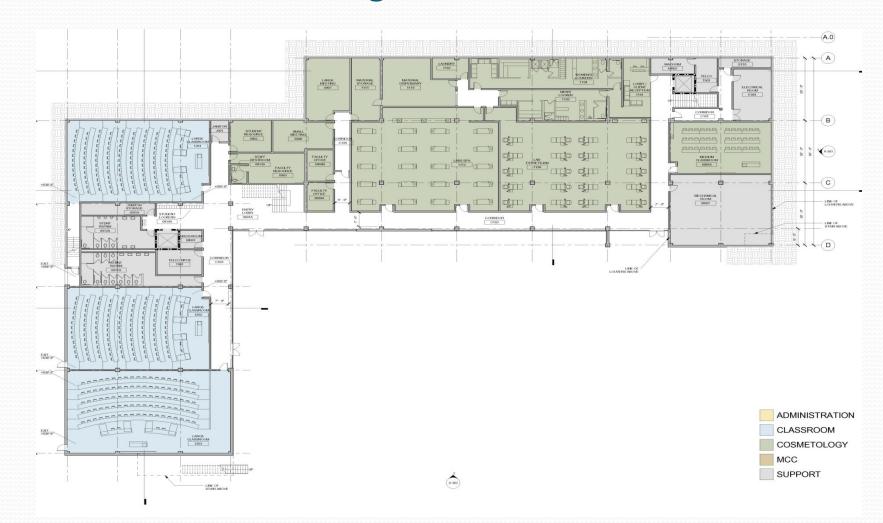


Building 4N: Second Floor

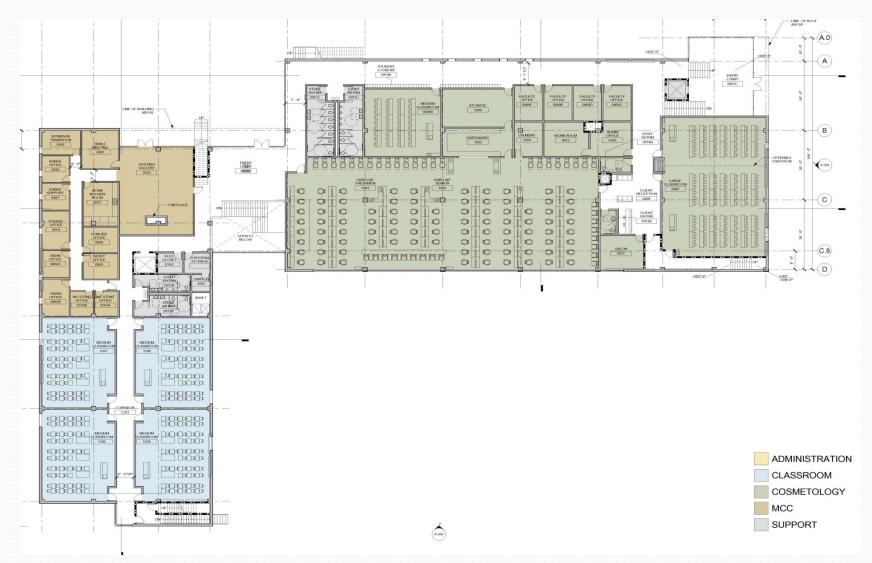



Building 4N: Third Floor

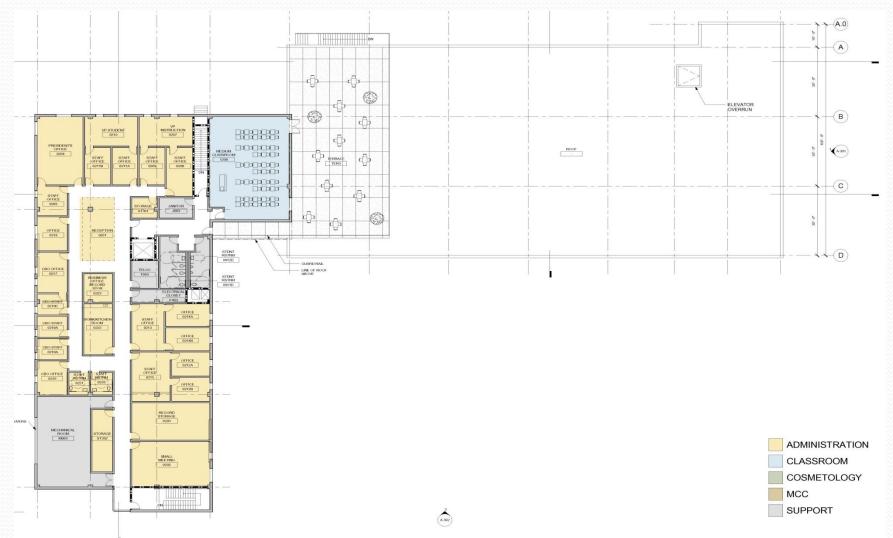

Building 11N: Auto Transmission

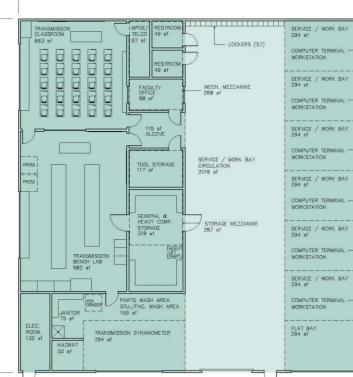



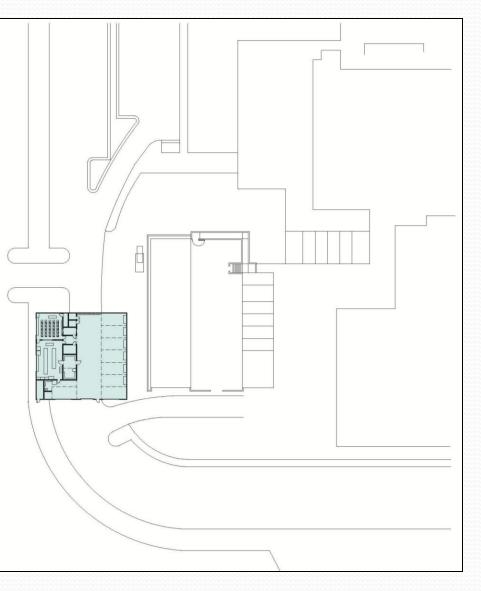

Sitework Improvements



O't-t_=

Skyline College CIP2 Design Build Project Schedule*

ID	0	Task Name	Duration	Start	Finish		2nd Half		JJASOND					1st Half								1st Half D.J.FMAM	
1							<u>, 191919</u>	A la lank right		A li lizis rizile				v i my only		alı huk dula		ele li ini vini d		V I ITT SITT	e no on	olo h mi quli	<u>• • • • • • • •</u>
2		SKY DESIGN-BUILD PROJECT	838 days	Thu 2/7/08	Mon 4/25/11	1		—				101010		s e	ky design	BUILD PR	DJECT						
3		Design Period	278 days	Thu 2/7/08	Mon 3/2/09	9		—		Desi	gn Period												
4		New B4N - Cosmetology, Administration and Wellness	278 days	Thu 2/7/08	Mon 3/2/09	9				New E	4N - Cosme	tology, Adr	ninistration	and Wellne	SS								
5		New B11N - Auto Transmission	153 days	Thu 5/1/08	Mon 12/1/08	8				New B11N -	Auto Trans	mission											
6		Sitework	153 days	Thu 5/1/08	Mon 12/1/08	8				Sitework													
7	1	Construction	546 days	Mon 3/23/09	Mon 4/25/11	1				-				- •	onstruction								
8	1	New B4N - Cosmetology, Administration and Wellnes	480 days	Tue 6/23/09	Mon 4/25/11	1								N	ew B4N - Co	smetology	, Administra	ation and We	ellness				
9		Construction	420 days	Tue 6/23/09	Mon 1/31/11	1								Constru	ction								
10	1	Group II FF&E installation	40 days	Tue 2/1/11	Mon 3/28/11	1								Grou	ıp II FF&E ir	nstallation							
11		Commissioning & Faculty/Student transitioning	20 days	Tue 3/29/11	Mon 4/25/11	1								Co	mmissionin	g & Faculty	//Student tra	ansitioning					
12	1	New B11N - Auto Transmission	195 days	Mon 4/27/09	Fri 1/22/10	0				-		New B1	11N - Auto Ti	ransmissior	1								
13		Construction	135 days	Mon 4/27/09	Fri 10/30/09	9					C (onstruction											
14		Group II FF&E installation	40 days	Mon 11/2/09	Fri 12/25/09	9						Group II F	F&E installa	tion									
15	1	Commissioning & Faculty/Student transitioning	20 days	Mon 12/28/09	Fri 1/22/10	0						Commis	sioning & Fa	aculty/Stude	ent transitio	ning							
16		Site Improvements	365 days	Mon 3/23/09	Fri 8/13/10	0				-			Site In	nprovement	S								
17		Phase I	105 days	Mon 3/23/09	Fri 8/14/09	9					Phase												
18		Phase 2	110 days	Mon 3/15/10	Fri 8/13/10	0							Phase	2									

*Dates subject to change

Question & Answer

http://www.smccd.edu/accounts/smccd/departments/facilities/

Linda da Silva Executive Director Construction Planning (650) 358-6726 <u>dasilva@smccd.edu</u>



"Building Today for Education Tomorrow"
