



Building 5 Dining Room Modernization — RFP 076

Cañada College

Mandatory Pre-Bid Conference






- LINDA DA SILVA, EXECUTIVE DIRECTOR, FACILITIES PLANNING DEPARTMENT
- BARRY CHIN, DESIGN MANAGER, FACILITIES PLANNING DEPARTMENT
- PEPPER POWELL, PROJECT COORDINATOR BIDDING
- STEVE OPSON, PROJECT COORDINATOR TECHNICAL
- José Nuñez, Vice Chancellor of Facilities
- Danny Glass, Facilities Operations Manager, Cañada College
- Jozsef Veres Chief Engineer, Cañada College
- ELIZABETH WITT, PROJECT ARCHITECT, BCA ARCHITECTS
- NIK SERNANDE, ARCHITECT, BCA ARCHITECTS
- LINDA RIZZOLI, SWINERTON MANAGEMENT & CONSULTING
- (Construction Manager)
- CIS INC. (INSPECTOR OF RECORD)






MEET THE TEAM



- WELCOME AND INTRODUCTIONS
- PREBID CONFERENCE ADMINISTRATION
- BID & CONTRACT AWARD SCHEDULE
- PROJECT OVERVIEW
- WORK SEQUENCE
- OCCUPIED CAMPUS COORDINATION REQUIREMENTS
- BID & CONTRACT DOCUMENTS
- QUESTION & ANSWER







- MANDATORY CONFERENCE (ATTENDANCE IS REQUIRED FOR PRIME BIDDERS):
 - -AUGUST 25, 2011 2:30 PM
 - -PLEASE SIGN IN
- PREBID CONFERENCE ATTENDANCE RECEIPT







- Mandatory PreBid Conference: Thursday, August 25, 2011
- PLANS AVAILABLE: SEPTEMBER 8, 2011
- LAST DAY FOR WRITTEN RFI'S: FRIDAY, SEPTEMBER 23, 2011
- LAST DAY THAT ADDENDA WILL BE ISSUED: WEDNESDAY, SEPTEMBER 28, 2011
- BIDS DUE @ CSM BUILDING 12: OCTOBER 4 @ 2:00 P.M.
- SMCCCD Board of Trustees Meeting (anticipated Contract APPROVAL): October 26, 2011
- ANTICIPATED SUBSTANTIAL COMPLETION: APRIL 6, 2012







BID & CONTRACT AWARD SCHEDULE MAJOR MILESTONES





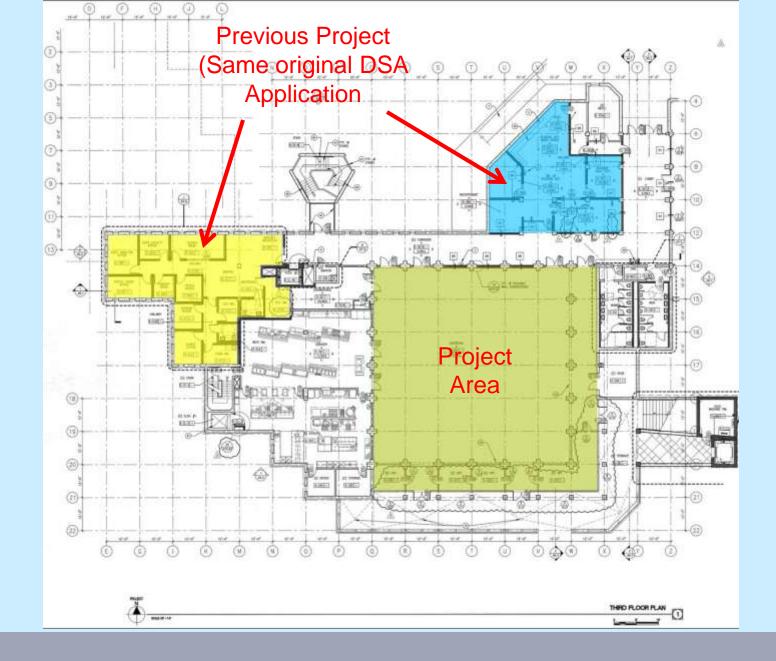



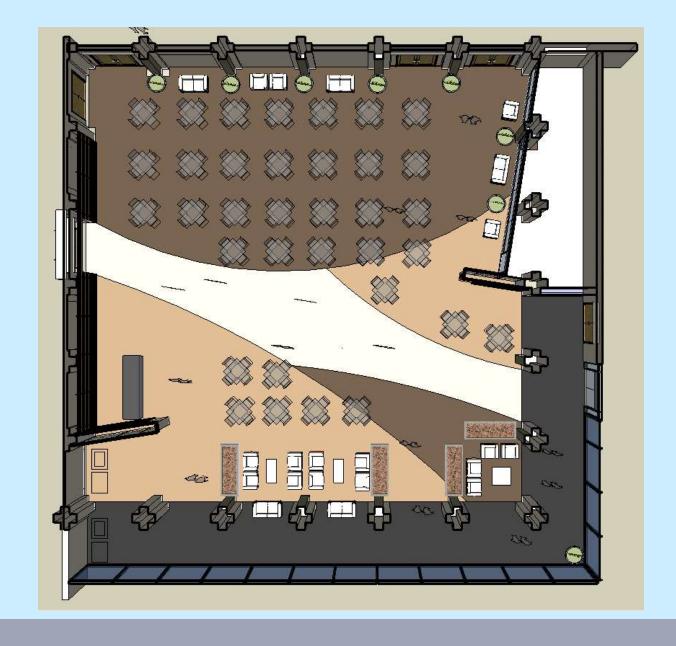














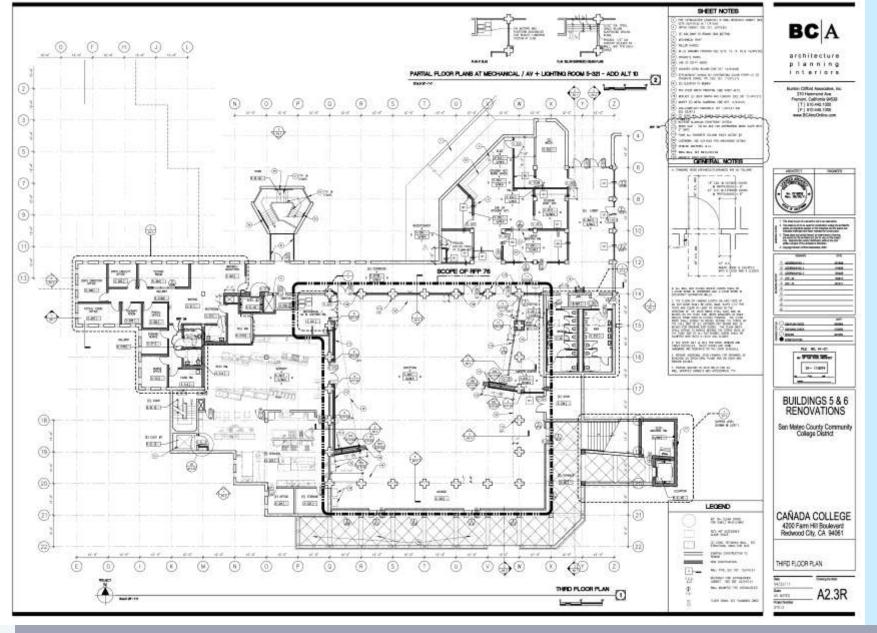




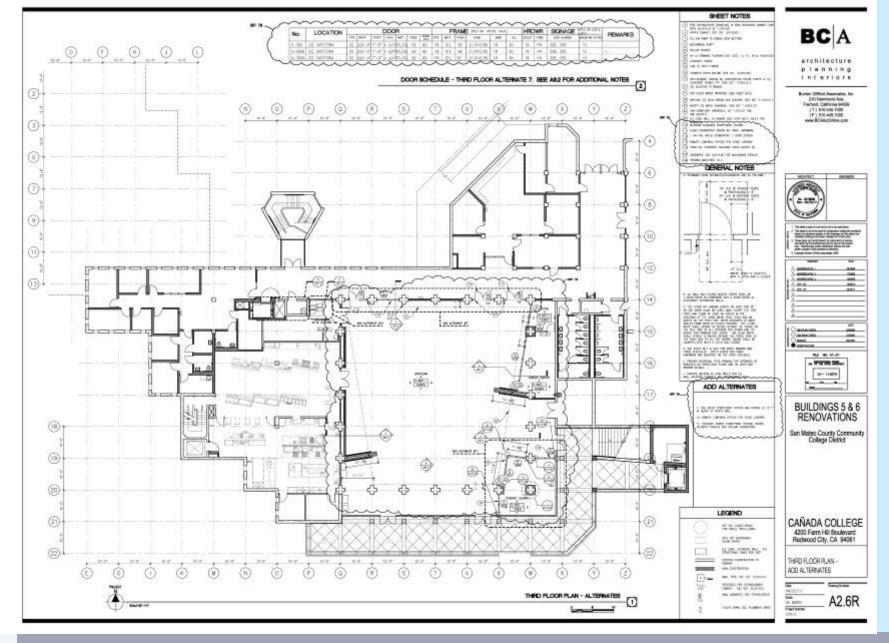



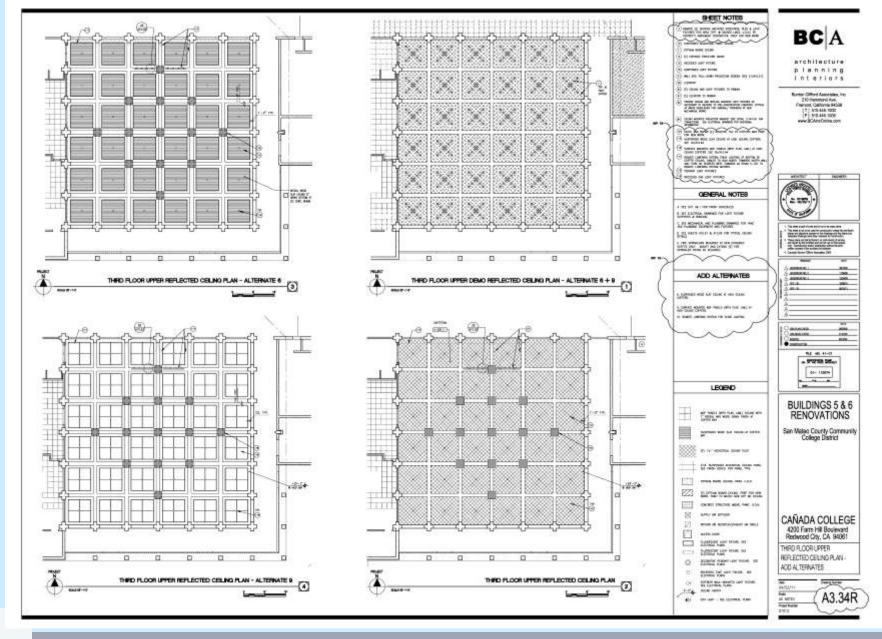



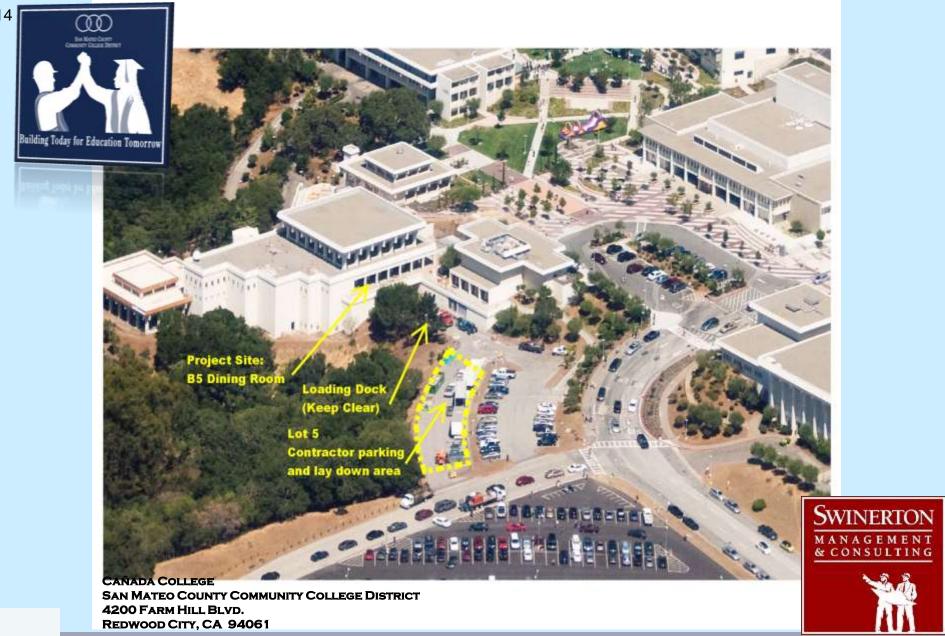







CONCURRENT CONSTRUCTION ALERT AND EVENTS


FINALS:

DECEMBER 12, 2011 TO DECEMBER 17,2011

CAMPUS POWER DOWN:


DECEMBER 19, 2011 TO JANUARY 2, 2012





- CAÑADA COLLEGE IS AN OCCUPIED CAMPUS
- COLLEGE EDUCATIONAL MISSION IS PARAMOUNT
- CONSTRUCTION LOGISTICS MUST ACCOMMODATE THE COLLEGE'S SCHEDULE, EVENTS AND PRIORITIES
- COMMUNICATION WITH CONSTRUCTION MANAGER
- WEEKLY OWNER/ARCHITECT/CONTRACTOR MEETING
- CONCURRENT PROJECT COORDINATION
 - PROTECT EXISTING UTILITIES
 - STUDY As-BUILTS
 - FIELD REVIEW WITH CHIEF ENGINEER
- ADVANCE NOTICE UTILITY SHUTDOWNS/ACCESS INTERRUPTIONS
- SIGNAGE TRAFFIC CONTROL/PEDESTRIAN RE-DIRECT
- CONTRACTOR PARKING PARKING LOT 5, WEST ROW
- STAGING AND LAYDOWN AREAS PARKING LOT 5, WEST ROW
- SAFETY —

LOCAL WORK AREA ENCLOSURE FENCING
SITE SAFETY SIGNAGE
GC POINT OF CONTACT ON SITE — AT ALL TIMES





OCCUPIED CAMPUS LOGISTICS




- Project documents are available at ARC NorCal (formerly Elite Reprographics) for a fee
 - (415)957-1234 or http://www.eliterepro.com/
- Also available at the District project website at:
- http://www.smccd.edu/accounts/smccd/departments/facilities/ /CanDiningRoom.shtml
- Bay Area Plan rooms





BID DOCUMENTS



THANK YOU

FOR YOUR INTEREST

IN OUR

CAPITAL IMPROVEMENT PROGRAM!

HTTP://WWW.SMCCD.EDU/ACCOUNTS/SMCCD/DEPARTMENTS/FACILITIES/





QUESTIONS & ANSWERS
